



**US Army Corps
of Engineers®**

**Restoration Advisory Board Update
Camp Croft Formerly Used Defense Site
Spartanburg, South Carolina
9 November 2023**



The US Army Corps of Engineers (USACE) is providing an update for the Camp Croft FUDS to the Restoration Advisory Board (RAB) in lieu of conducting the RAB meeting in person. This update summarizes progress at the Camp Croft FUDS since the RAB meeting in August 2023.

1. Project 03 Munitions Debris Area and Project 05 Range Complex Remaining Lands:

The remedy identified in the January 2019 Decision Document (DD) consisting of public education for Projects 03 and 05 has been implemented. The public education tools implemented consists of signage and educational materials, to enhance the community's understanding of site conditions. Educational materials (brochures) were provided to Croft State Park and are located at the visitor center. The remedial action was implemented in June 2020 and USACE evaluated the remedial action to ensure it provides protection to the public with the first five-year review (FYR) completed in September 2023. The FYR concluded the remedies implemented at Projects 03 and 5 currently protect human health and the environment. However, for the remedy to be protective in the long-term, the current remedy status of each project area and educational materials should be provided to the Spartanburg County department(s) that issue building and land disturbance permits to distribute when permits are issued to landowners with the former Camp Croft.

2. Project 07 Maneuver Area/Croft State Park:

The remedy identified in the September 2019 Decision Document (DD) consists of Advanced Geophysical Classification & Analog supported Surface and Subsurface Munitions Removal, Long Term Management (LTM) and Public Education (3Rs Program). Signs similar to those produced for Projects 03 and 05 were installed within the Project 07 boundaries and additional brochures were produced for distribution.

A contract to execute the remedial action (RA) at the Camp Croft FUDS Project 07 munitions response site (MRS) was awarded in April 2020 and additional modifications (for additional acreage) were awarded in August 2021 and June 2022. However, a partial work stop order was implemented on 2 May 2023 due to project scope and site condition changes and inability to add additional acres under the task order. MEC items recovered during the RA field activities were disposed on 4 August 2023. Contractor is completing the remaining tasks under the partial work stop order and demobilized from the field in August 2023. Progress for the various tasks for the funded acreage at Project 7 is shown in Table 1 and illustrated in Figures 2 and 3. MEC item locations are also illustrated in Figures 2 and 3.

A task order is planned to be awarded in March 2024 to complete the remainder of the field work for the remedial action. Under the current contract, geophysical data is being process and the RA report is being prepared and is tentatively scheduled to be finalized in April 2024.

Archaeological confirmation that items/sites discovered do not contain an archaeological significance is being conducted throughout the RA process.

3. Next RAB Meeting

The next RAB meeting is tentatively scheduled for February 1, 2024. USACE will continue to coordinate with the Camp Croft RAB members regarding conducting RAB meetings and provide project updates as needed.

TABLES

Table 1: Task Status for Funded Areas (as of 10 October 2023)

Task	Funded Acreage (717 acres)
Surface MEC Clearance	100%
PLS Survey	100%
Vegetation Clearance	100%
AGC Survey	97%
Intrusive	44%

Table 2: MEC Items Discovered During Project 07 RA (as of 2 November 2023)

MEC Item	Date	Activity/Location
<p>1. M17A1 Rifle Grenade/Signal Flare</p> 	<p>4/12/21</p>	<p>Surface MEC Clearance (BH29)</p>
<p>2. MK II Hand Grenade</p> 	<p>5/3/21</p>	<p>Surface MEC Clearance (BP40)</p>
<p>3. MK II High Explosive (HE) Grenade</p> 	<p>10/26/21</p>	<p>Surface MEC Clearance (Grid BH15)</p>
<p>4. 60 mm H49 HE Mortar</p> 	<p>11/8/21</p>	<p>Surface MEC Clearance (Grid CZ77)</p>

Table 2: MEC Items Discovered During Project 07 RA (as of 2 November 2023) continued

MEC Item	Date	Activity/Location
<p>5. M49 Trip Flare</p> 	<p>12/1/21</p>	<p>Surface MEC Clearance (Grid EE121)</p>
<p>6. MK II HE Grenade</p> 	<p>5/21/22</p>	<p>Found by camper (Grid ED105)</p>
<p>7. M17A1 Rifle Grenade Flare</p> 	<p>5/31/22</p>	<p>Intrusive Operations (Grid CK23)</p>
<p>8. 60 mm HE Mortar</p> 	<p>8/31/22</p>	<p>Intrusive Operations (CG49)</p>

Table 2: MEC Items Discovered During Project 07 RA (as of 2 November 2023) continued

MEC Item	Date	Activity/Location
<p>9. 60mm HE Mortar</p> 	<p>9/15/22</p>	<p>Intrusive Operations (AI11)</p>
<p>10. 60mm HE Mortar</p> 	<p>9/20/22</p>	<p>Intrusive Operations (AK11)</p>
<p>11. M1 Fuze</p> 	<p>9/23/22</p>	<p>Intrusive Operations (AK8)</p>
<p>12. 60mm M49 Mortar</p> 	<p>1/11/23</p>	<p>Intrusive Operations (DZ121)</p>

Table 2: MEC Items Discovered During Project 07 RA (as of 2 November 2023) continued

MEC Item	Date	Activity/Location
13. 60mm M49 Mortar 	1/17/23	Intrusive Operations (DZ124)
14. 60mm M49 Mortar 	1/19/23	Intrusive Operations (DX124)
15. 60mm M49 Mortar 	1/19/23	Intrusive Operations (DX124)
16. MK II Practice Hand Grenade 	1/23/23	Intrusive Operations (ED107)

Table 2: MEC Items Discovered During Project 07 RA (as of 2 November 2023) continued

MEC Item	Date	Activity/Location
17. MK II HE Hand Grenade 	1/30/23	Intrusive Operations (DV108)
18. MK II HE Hand Grenade 	1/30/23	Intrusive Operations (DX105)
19. MK II HE Hand Grenade 	1/30/23	Intrusive Operations (DV106)
20. MK II HE Hand Grenade 	1/30/23	Intrusive Operations (DV106)

Table 2: MEC Items Discovered During Project 07 RA (as of 2 November 2023) continued

MEC Item	Date	Activity/Location
21. 60mm M49 HE Mortar 	2/14/23	Intrusive Operations (DH114)
22. 60mm M49 HE Mortar 	2/14/23	Intrusive Operations (DH116)
23. 60mm M49 HE Mortar 	3/3/23	Intrusive Operations (CZ78)
24. MK II HE Hand Grenade 	3/16/23	Intrusive Operations (BO24)

Table 2: MEC Items Discovered During Project 07 RA (as of 2 November 2023) continued

MEC Item	Date	Activity/Location
<p>25. 81mm M43 HE Mortar</p> 	<p>3/24/23</p>	<p>Intrusive Operations (DL109)</p>
<p>26. 60mm M49 HE Mortar</p> 	<p>3/24/23</p>	<p>Intrusive Operations (DL105)</p>
<p>27. 60mm M49 HE Mortar</p> 	<p>4/6/23</p>	<p>Intrusive Operations (CZ73)</p>
<p>28. 60mm M49 HE Mortar</p> 	<p>4/17/23</p>	<p>Intrusive Operations (DO113)</p>

Table 2: MEC Items Discovered During Project 07 RA (as of 2 November 2023) continued

MEC Item	Date	Activity/Location
<p>29. MK II HE Grenade</p> 	<p>6/27/23</p>	<p>Intrusive Operations (DS104)</p>
<p>30. MK II HE Grenade</p> 	<p>6/27/23</p>	<p>Intrusive Operations (DY135)</p>

FIGURES

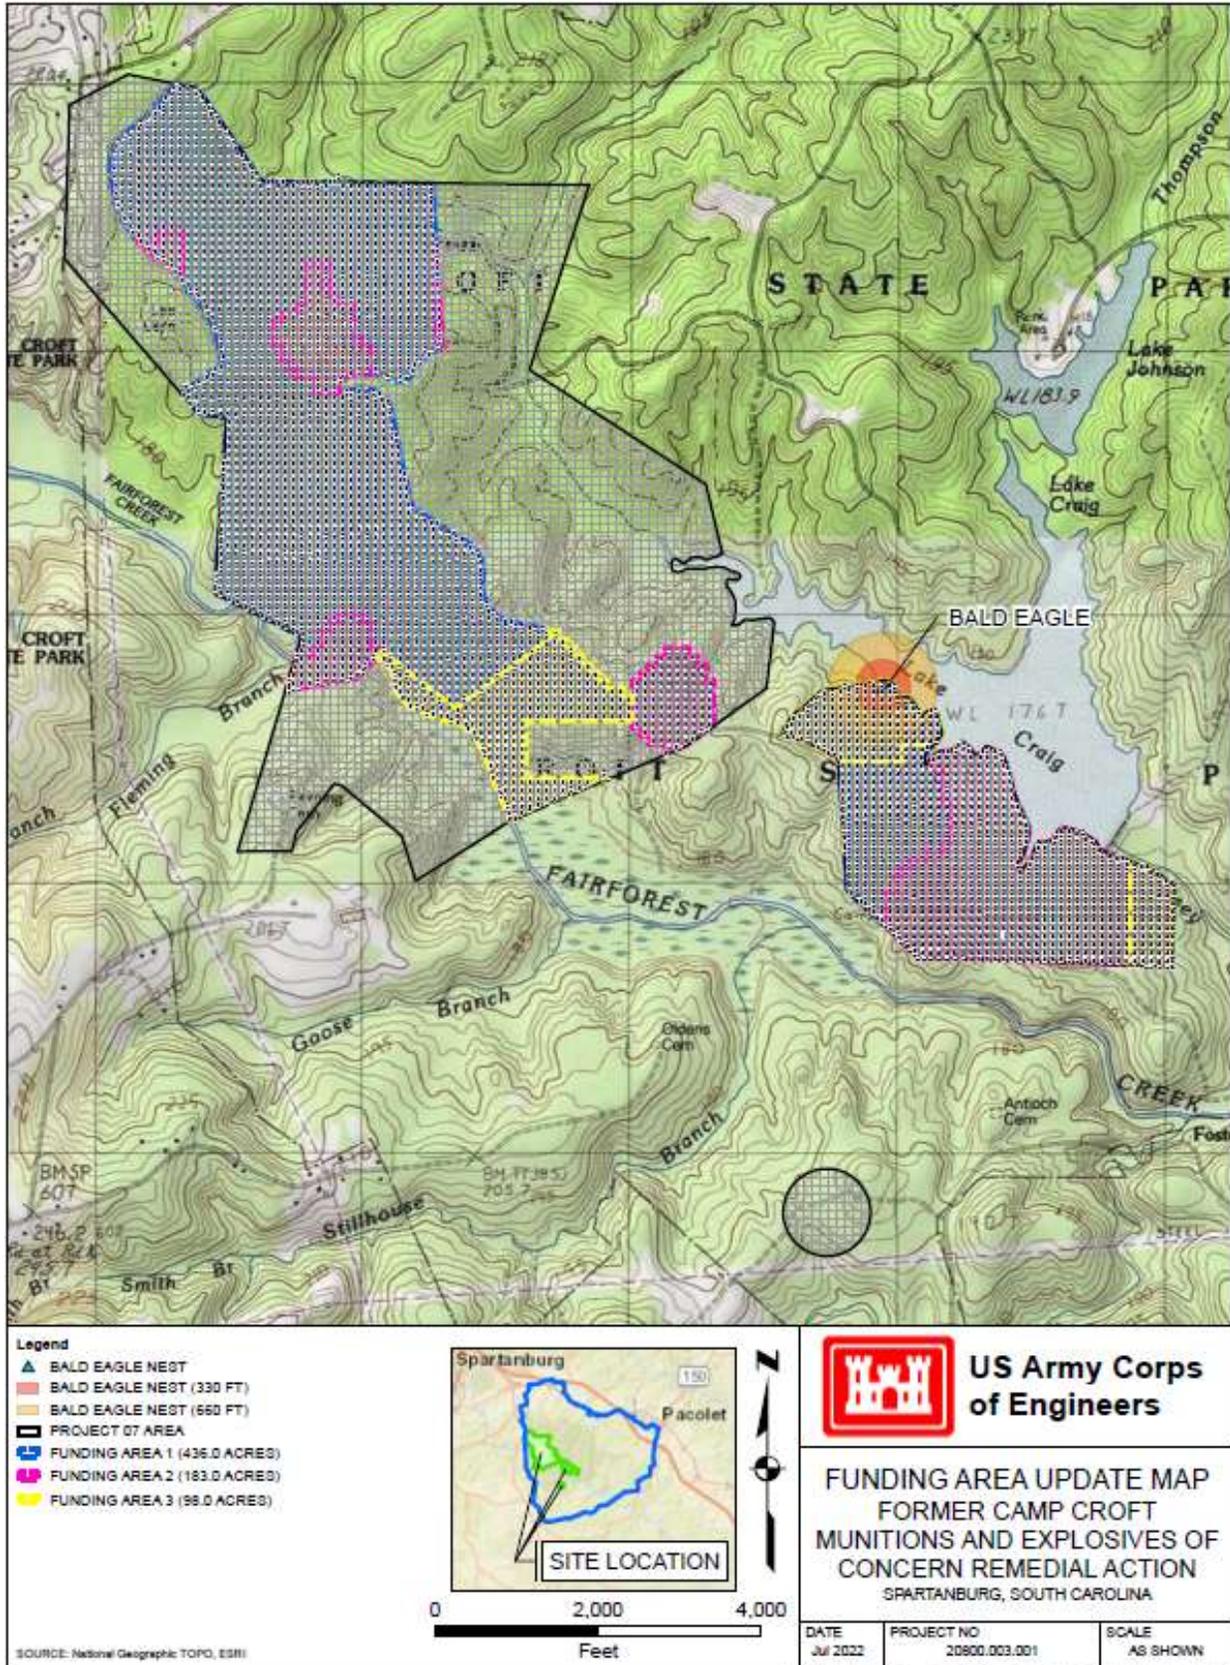


Figure 1: Project 07 Boundaries

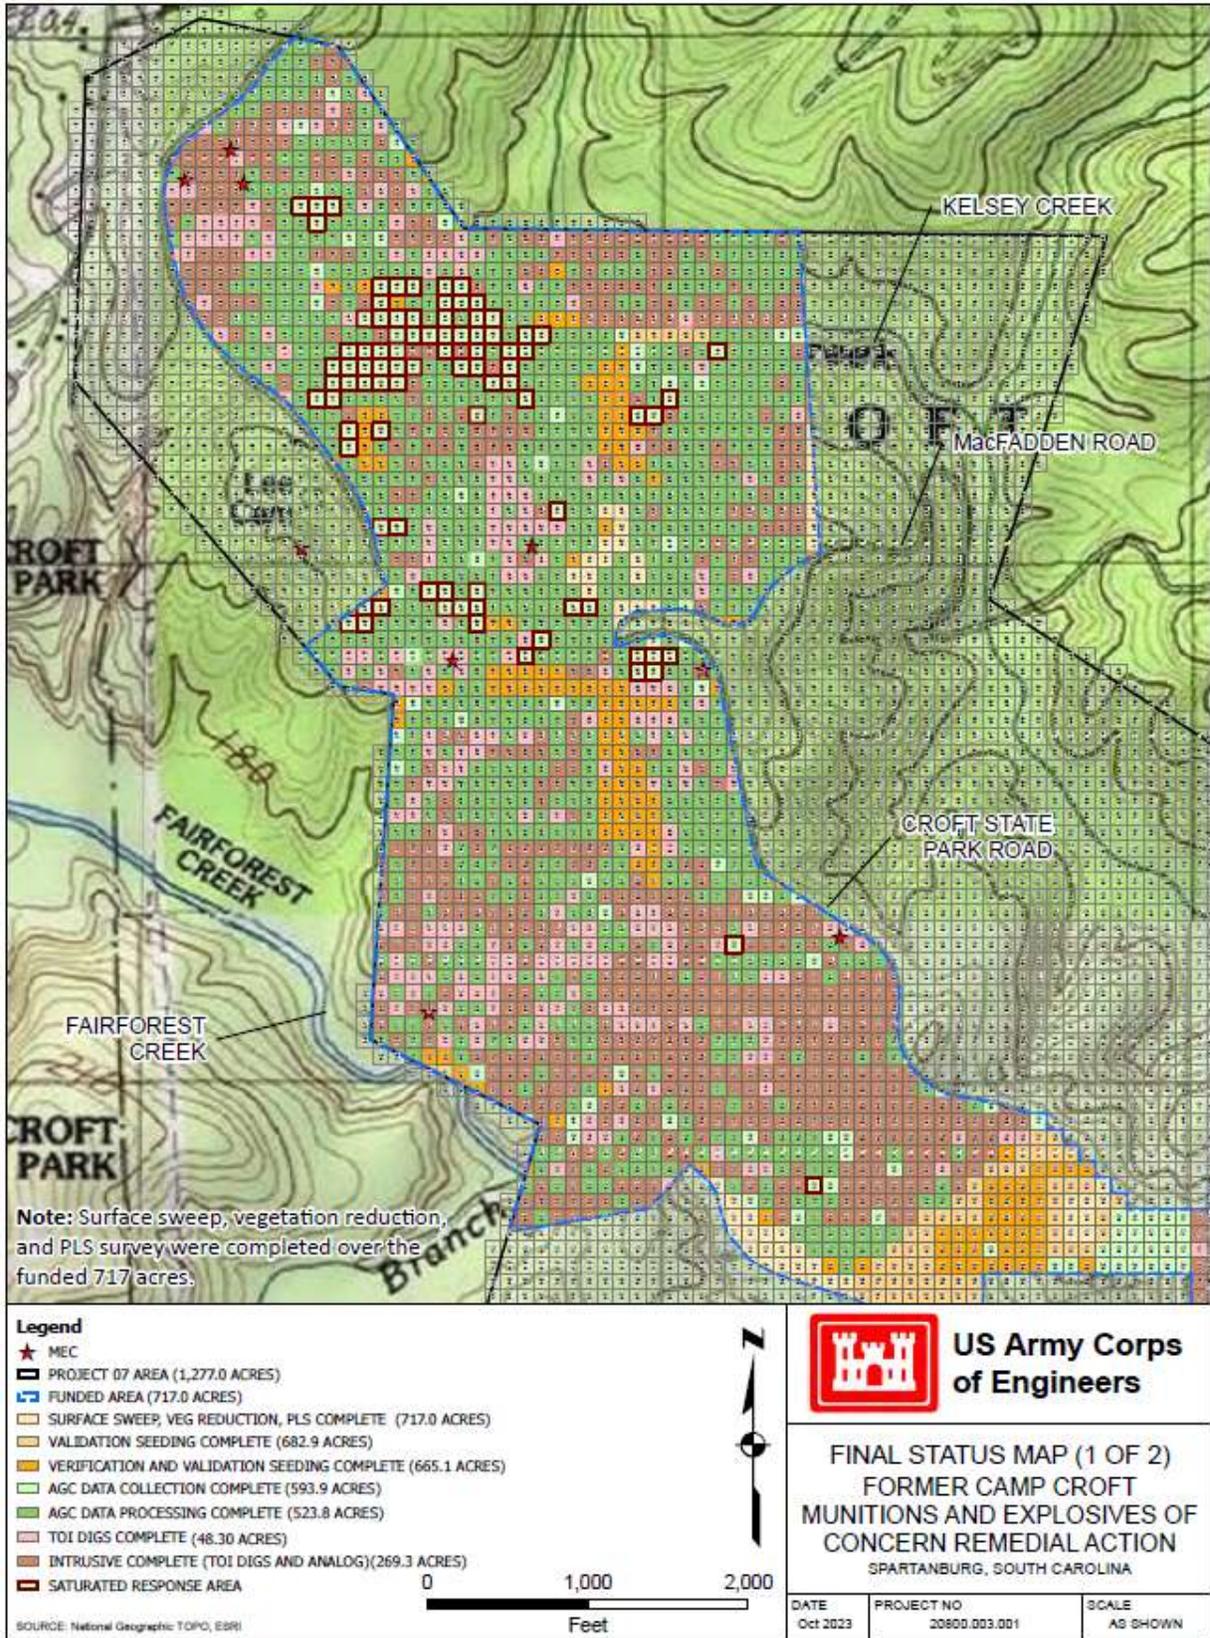


Figure 2: Project 07 RA Status (1 of 2)

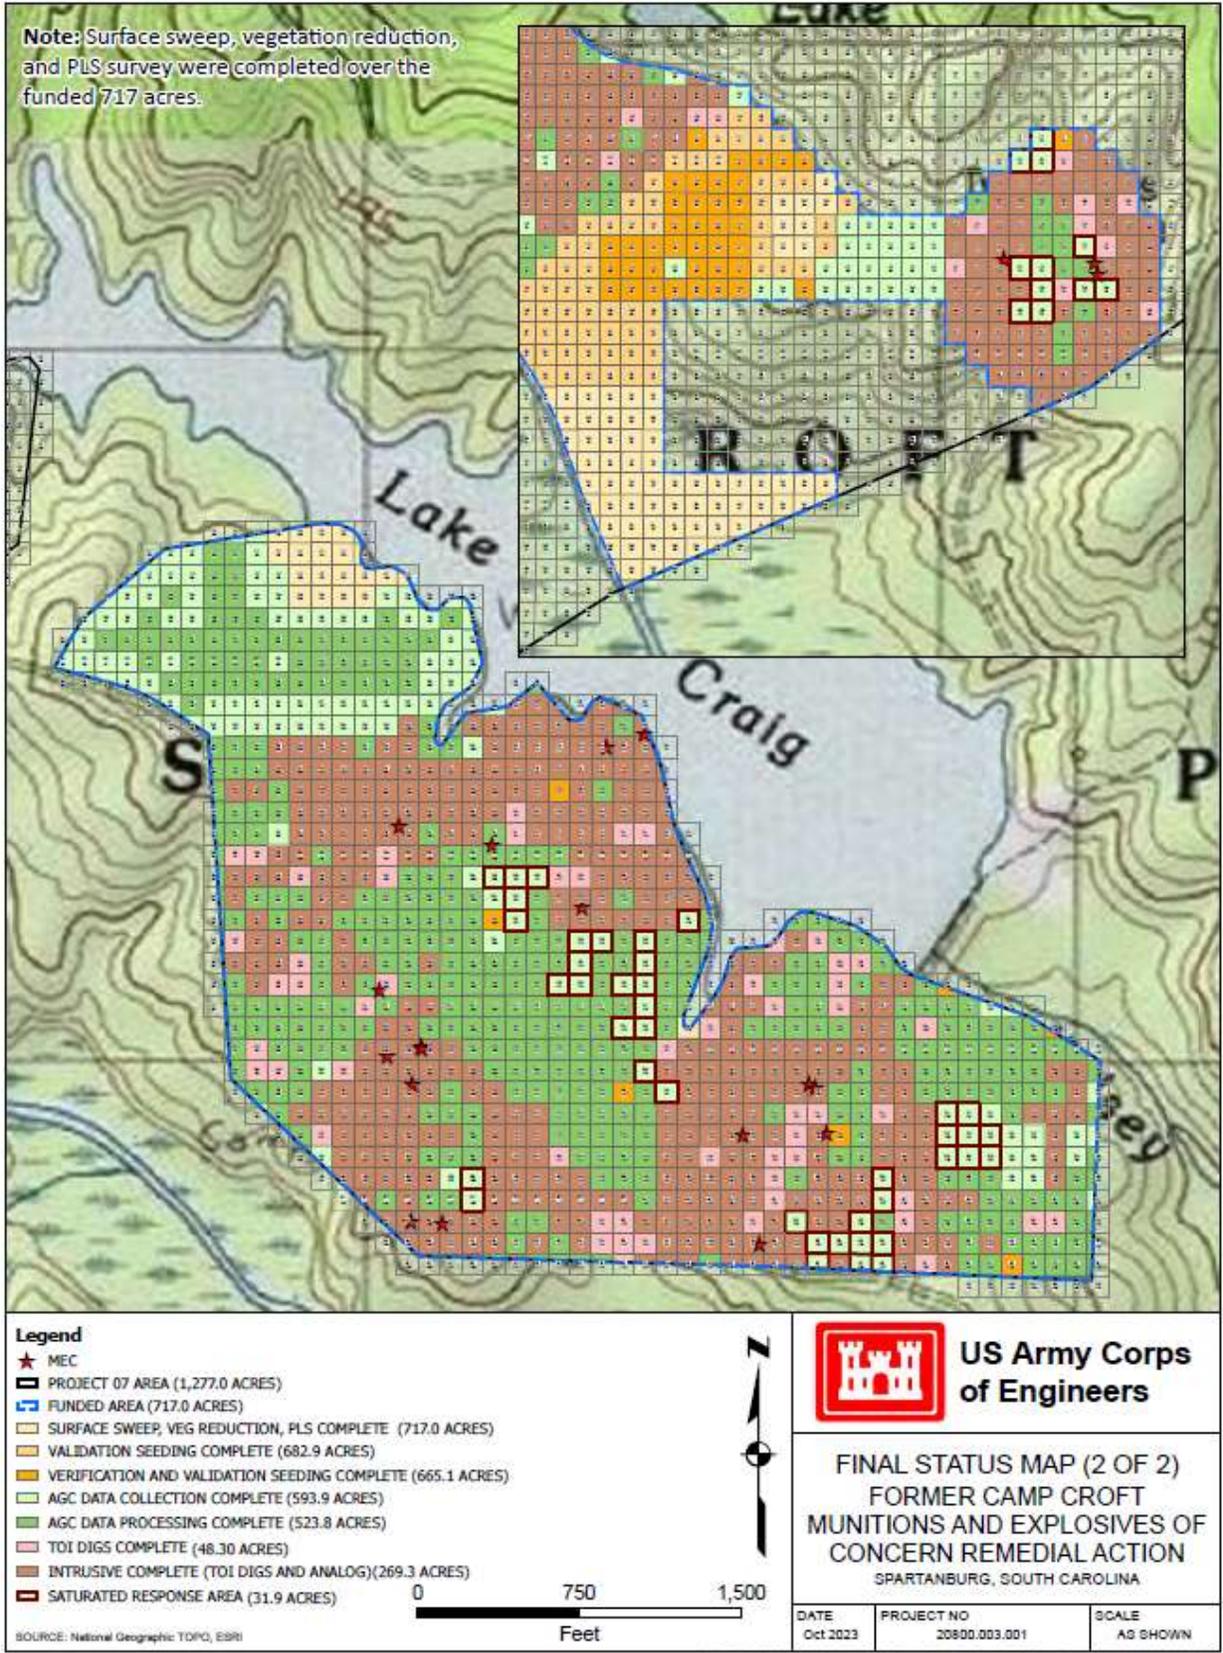


Figure 3: Project 07 RA Status (2 of 2)
